


PROJECT SCHEDULE  
 CH2M HILL, INC.  
 Collin County Outer Loop: DNT to East of SH 289

ID	Task Name	Duration	Predecessors	Start	Finish	Feb '13	Mar '13	Apr '13	May '13	Jun '13	Jul '13	Aug '13	Sep '13	Oct '13	Nov '13
1	Contract NTP	1 day		Mon 3/4/13	Mon 3/4/13										
2	<b>Develop Schematic Layout</b>	<b>167 days</b>	<b>1</b>	<b>Tue 3/5/13</b>	<b>Wed 10/23/13</b>										
3	Aerial & Field Survey	65 days	1	Tue 3/5/13	Mon 6/3/13										
4	Hydrologic and Hydraulic Investigation	45 days	3FS-15 days	Tue 5/14/13	Mon 7/15/13										
5	Develop Preliminary Hydraulic Report	20 days	4FS-20 days	Tue 6/18/13	Mon 7/15/13										
6	Develop Preliminary Schematic	65 days	3	Tue 6/4/13	Mon 9/2/13										
7	Submit Preliminary Schematic and Hyrdraulic Report	1 day	5,6	Tue 9/3/13	Tue 9/3/13										
8	Collin County Review	10 days	7	Wed 9/4/13	Tue 9/17/13										
9	Develop Final Schematic and Hyrdraulic Report	25 days	8	Wed 9/18/13	Tue 10/22/13										
10	Submit Final Schematic and Hydralic Report	1 day	9	Wed 10/23/13	Wed 10/23/13										

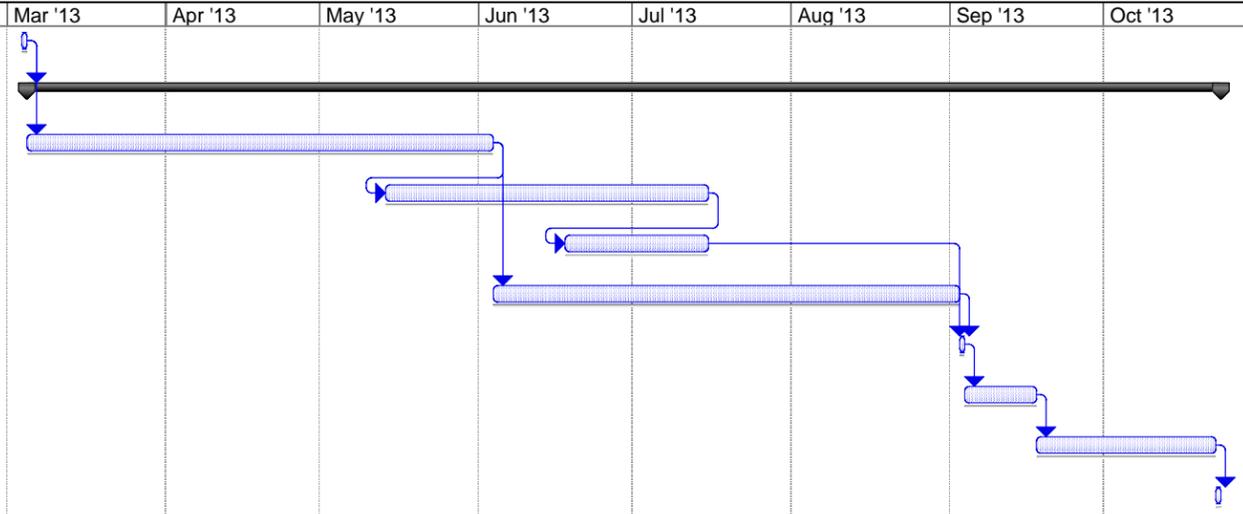

Project: CCOL 3 Schematics Schedule  
 Date: Wed 1/23/13

Task		Progress		Summary		External Tasks		Deadline	
Split		Milestone		Project Summary		External Milestone			
