

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Feb 8, '26										
								T	W	T	F	S	S	M	T	W		
1		Submittal Approvals	3 days	Mon 3/2/26	Wed 3/4/26													
2		Order Fixtures and R Panel	1 day	Thu 3/5/26	Thu 3/5/26													
3		Mobilization	2 days	Mon 3/16/26	Tue 3/17/26													
4		Power Wash Walls	3 days	Fri 3/20/26	Tue 3/24/26													
5		RR Fixtures Demo	1 day	Mon 3/23/26	Mon 3/23/26													
6		Remove and Replace Plumbing in chase	4 days	Tue 3/24/26	Fri 3/27/26	5												
7		Installation of Purlins/Angle Iron	3 days	Wed 3/25/26	Fri 3/27/26	4												
8		Insulation	6 days	Mon 3/30/26	Mon 4/6/26	7												
9		Concrete Grinding and Sealing	2 days	Mon 3/30/26	Tue 3/31/26	6												
10		Installation of New Toilets and Sinks	3 days	Wed 4/1/26	Fri 4/3/26	9												
11		Installation of R Panel	7 days	Tue 4/7/26	Wed 4/15/26	8												
12		Installation of New Drinking Fountain	1 day	Mon 4/6/26	Mon 4/6/26	10												
13		G2 Punch Walk	1 day	Thu 4/16/26	Thu 4/16/26	12												
14		Address Punch Items	3 days	Thu 4/16/26	Mon 4/20/26	13												
15		Collin County Punch Walk	1 day	Mon 4/20/26	Mon 4/20/26	14												


Project: Show Barn Insulation a Date: Thu 2/26/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Feb 8, '26									
								T	W	T	F	S	S	M	T	W	
16		Address Punch Items	3 days	Tue 4/21/26	Thu 4/23/26	15											
17		Project Completion	1 day	Fri 4/24/26	Fri 4/24/26	16											

Project: Show Barn Insulation a Date: Thu 2/26/26


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

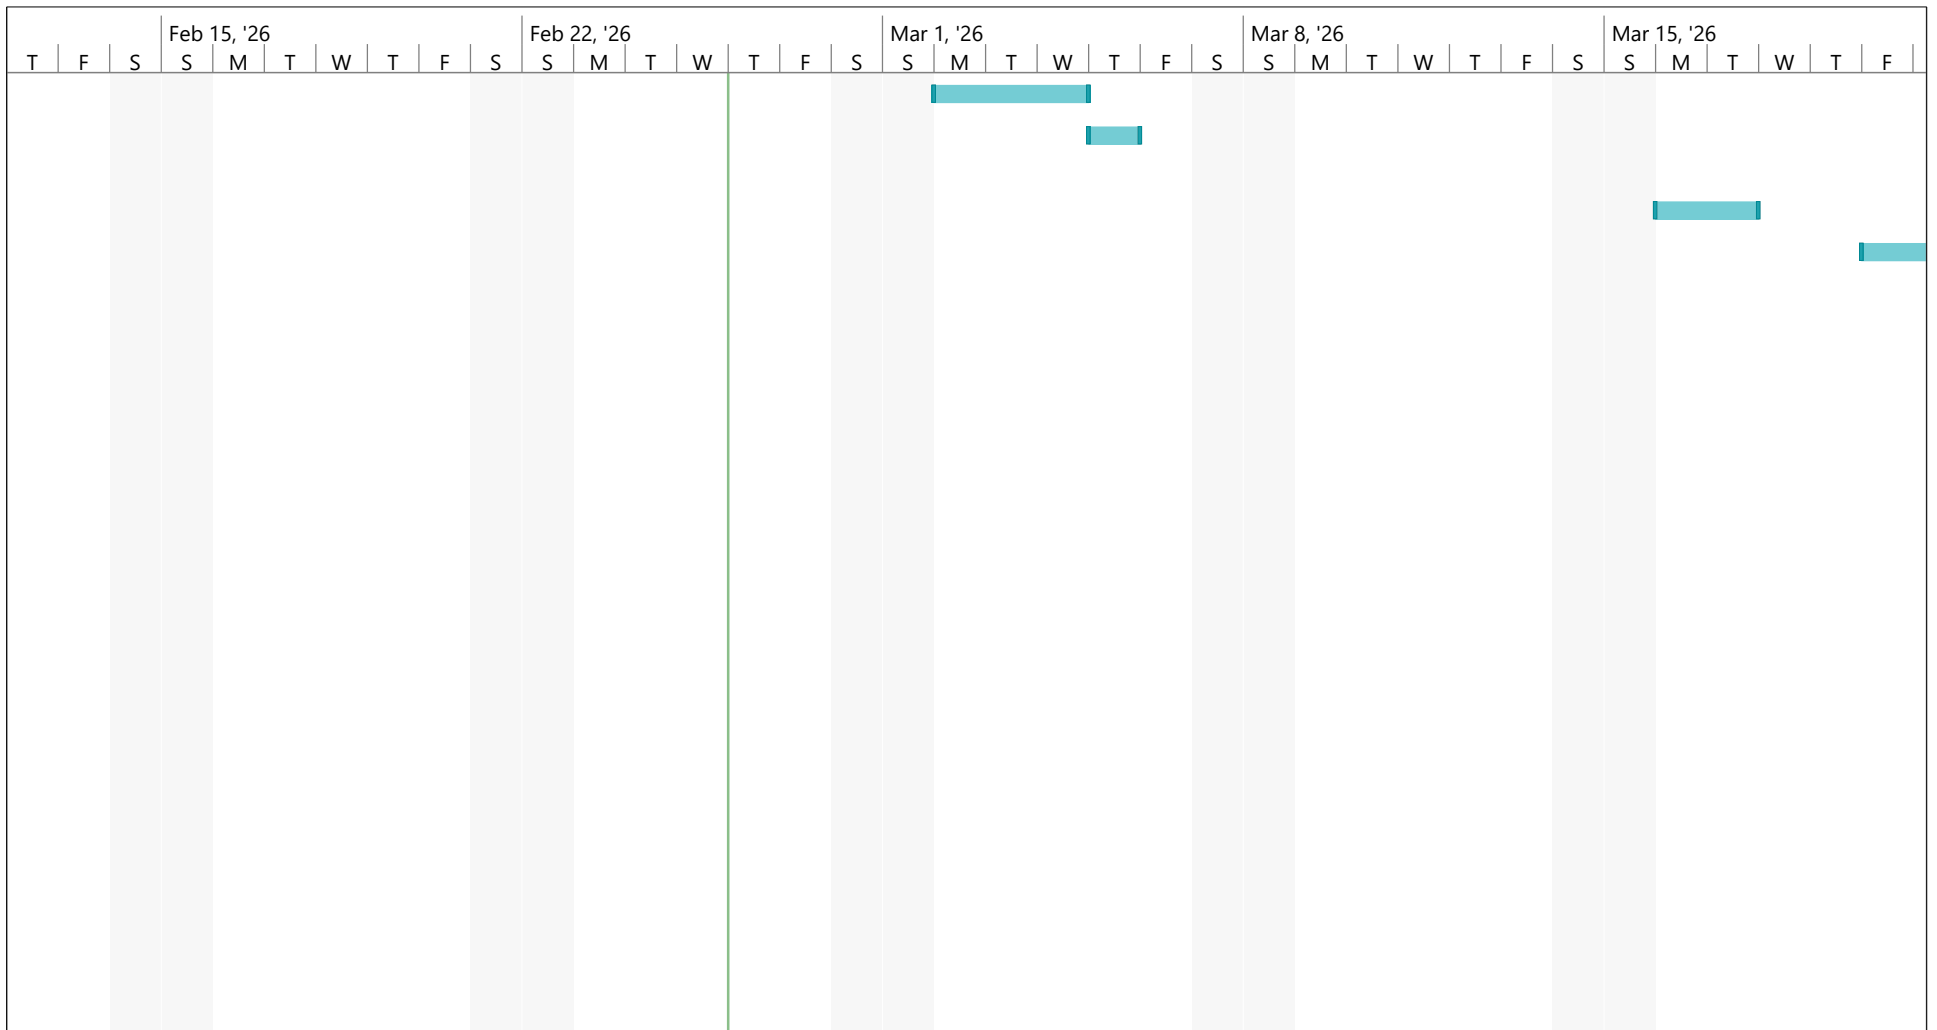


Project: Show Barn Insulation a
Date: Thu 2/26/26



Project: Show Barn Insulation a Date: Thu 2/26/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

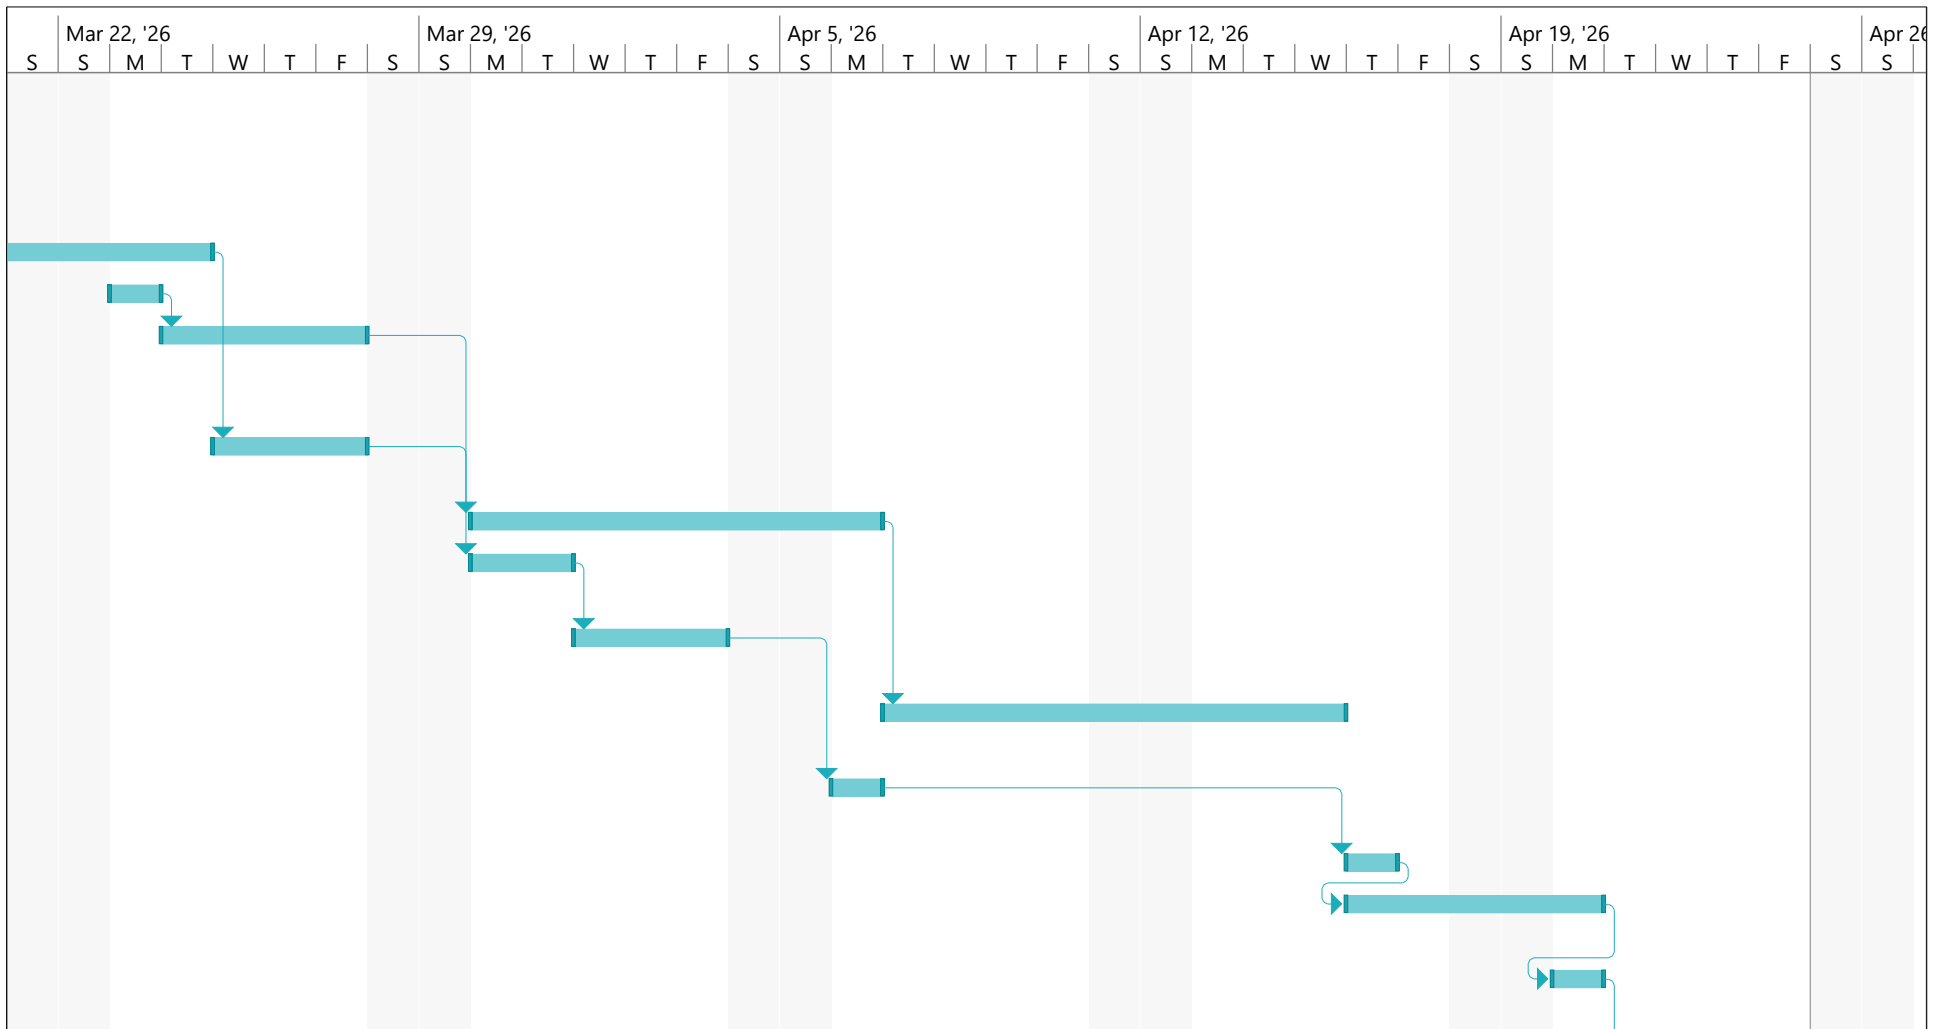

Project: Show Barn Insulation a Date: Thu 2/26/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



Project: Show Barn Insulation a Date: Thu 2/26/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			
