



Friday, September 29, 2006

Brian Nicodemus
PGAL
105 Decker Court, Suite 600
Irving, TX 75062

**RE: Potential Change Order 0103
Collin County Justice Center - 3090**

Dear Mr. Reese,

Hunt Construction Group (Hunt) respectfully requests your review and approval of the attached Potential Change Order (PCO) number **0103** as titled: **Vanity Support Wall Modifications per RFI # 376 & 381**. This change is required because the contract documents did not require in-wall steel supports at all locations. After it was confirmed that supports were required at all locations, portions of the walls had to be removed, furred, and replaced to accommodate installation of the vanity support system as required. Cost to complete the work is as follows:

Item	Contractor	Amount Proposed
001	Marek Brothers Systems, Inc.	\$4,003.00
002	Hunt Construction Group, Inc.	\$400.00

Total Amount: \$4,403.00

Please indicate your acceptance of this change by signing in the appropriate location below and forwarding to the Owner for review and execution. If you have any questions or need additional information, please contact Doug Workman or myself at your earliest convenience.

Sincerely,


LANDRY RAY
Project Engineer

Cc: Doug Workman
Hunt Construction Group



Architect signature

Owner signature

Hunt Construction Group, Inc.
Collin County Justice Center

2100 Bloomdale Road (75071), P.O. Box 1927, McKinney, Texas 75070
Phone: (972) 984-1440 Fax: (972) 984-1431 www.huntconstructiongroup.com



Marek Brothers Systems, Inc.

WORK ORDER

- 1233 LAKESHORE DRIVE • COPPELL, TEXAS 75019 • 972/393-4343
- 11003 IOTA DRIVE • SAN ANTONIO, TEXAS 78217-2609 • 210/657-4437
- 638 COMMERCIAL DRIVE • BUDA, TEXAS 78610 • 512/312-2756
- 3539 OAK FOREST DRIVE • HOUSTON, TEXAS 77018-6121 • 713/681-2626

DATE July 21-06
 MBS JOB NO. _____

CHARGE TO: HUNT

PROJECT: Collin Co. Justice Ctr.

CUSTOMER P.O./REF. NO: _____ LHI # _____ W.O. # _____ PR # _____

BRIEF DESCRIPTION AND LOCATION OF WORK: Adding 6" Chase walls - PER "ERIC"
MAREK WAS ASKED TO ADD WALLS AT RESTROOM VANITYS - TOTAL OF 12
L.I.L AND 1ST FLRS

QUANTITY	UNIT	DESCRIPTION OF MATERIAL	UNIT PRICE	EXTENSION	AUTHORIZATION FOR PAYMENT AND COMMENCEMENT OF EXTRA WORK
30 pcs		5/8 TILEBACKER 4x8 BOARD	33. ⁰⁰	1,008. ⁰⁰	 SIGNATURE _____ TITLE _____ DATE _____
7 BDLs		3 5/8 STUP X 10'	62. ⁸⁰	565. ²⁰	
4 "		3 5/8 TRK.	57. ⁵⁰	230. ⁰⁰	
	Rms	00110, 00108, 10110, 10112 10324, 10324 ONLY 6. Rms were Furred out There were 6 than the SheetRock was tore up due to installing Supports Angles Ct			TOTAL MAT'L. <u>\$1,803</u>

NAME	MON	TUE	WED	THU	FRI	SAT	SUN	TOTAL HOURS	RATE	EXTENSION
	7/17	7/18	7/19	7/20	7/21	X	X			
JUAN ARRISO	8	8	8	8	8			40	27. ⁵⁰	1,100. ⁰⁰
JOSE ARRISO	8	8	8	8	8			40	27. ⁵⁰	1,100. ⁰⁰

HOURS TO DATE _____
 WORK APPROVED AS COMPLETED SIGNATURE Work has been completed [Signature]

TITLE: Asst Supt DATE: 7/24/06 TOTAL LABOR \$2,200.⁰⁰

MAREK BROS. SYSTEMS Prank Hand TOTAL LABOR & MATERIAL \$4,003.⁰⁰

TITLE: _____ DATE: 7-21-06



Request for Information 376

Detailed, RFIs Grouped by RFI Number

Collin County Justice Center
2100 Bloomdale Rd.
McKinney, TX 75071

Project # 3090
Tel: (972) 984-1440 Fax: (972) 984-1431

Hunt Construction Group, Inc.

RFI #: 376 **Date Created: 8/5/2006**

Answer Company	Answered By	Author Company	Authored By
PGAL 105 Decker Court Suite 600 Irving, TX 75062	John Reese	Hunt Construction Group, Inc. 2100 Bloomdale Rd. McKinney, Texas 75071	Landry Ray

Co-Respondent	Author RFI Number
---------------	-------------------

Subject	Discipline	Category
Restroom Vanity Supports	Architectural	Clarification

Cc: Company Name	Contact Name	Copies	Notes
PGAL	Brian Nicodemus	1	
PGAL	Mike Huffman	1	

Question **Date Required: 8/12/2006**

Ref. A5.25:

Per general note at lower left corner of detail 10/A5.25, steel vanity supports are to be used "when perpendicular walls are not located at both ends of the counter."

1. Per field conversation between John Reese & Doug Workman, please confirm steel vanity supports may be used at all locations.
2. If not, please provide detail for installation where perpendicular walls are located at each end of the counter.

Suggestion

Answer **Date Answered:**

1. Steel vanity supports as shown on detail 10/A5.25 may be used at the Contractor's option, where space permits at all restroom locations.

John Reese, PGAL
8/16/06



Request for Information 381

Detailed, RFIs Grouped by RFI Number

Collin County Justice Center
2100 Bloomdale Rd.
McKinney, TX 75071

Project # 3090
Tel: (972) 984-1440 Fax: (972) 984-1431

Hunt Construction Group, Inc.

RFI #: 381

Date Created: 8/5/2006

Answer Company	Answered By	Author Company	Authored By
PGAL 105 Decker Court Suite 600 Irving, TX 75062	John Reese	Marek Brothers Systems, Inc. 12333 Lakeshore Drive Coppell, TX 75019	Bryant Hand

Co-Respondent

Author RFI Number

Subject	Discipline	Category
Restroom Vanity Support Clearances	Architectural	Field Condition

Cc: Company Name	Contact Name	Copies	Notes
PGAL	Brian Nicodemus	1	
Marek Brothers Systems, Inc.	Kenny LaDuke	1	

Question

Date Required: 8/12/2006

Ref. A5.25:

Gang restroom enlarged plan 2/A4.00 calls for a dimension of 9" at chase between lavatory counters. This is an insufficient amount of space to accommodate two (2) counter supports and a sanitary line as indicated in the attached sketch. This condition occurs at Restrooms: 00108, 00110, 10110, 10112, 10324, 10326, 20110, 20112, 20338, 20340, 30110, 30112, 30224, & 30226.

1. Per field conversations between John Reese, Eric Terry, & Shaune Hembrough, please confirm it is acceptable to furr the walls up to 3" at each restroom counter where this occurs.



Suggestion

Answer

Date Answered: 8/16/2006

1. The Contractor may, at his option, increase the plumbing chases per the Contractor's attached sketch in the Restrooms listed above. The walls perpendicular to the wet wall shall be checked to insure that there is sufficient room to allow for the installation of the recessed paper towel dispensers/disposals. Maintain a minimum of 1 1/2" clear (3" clear preferred) between: 1) the paper towel unit trim and the countertop, and 2) the paper towel unit trim and the end of the tile finish on the wall.

John Reese, PGAL
8/16/06

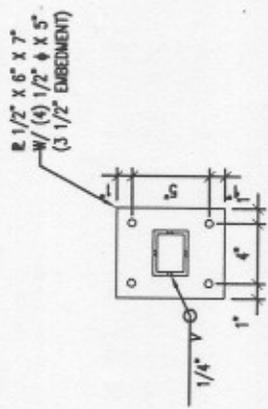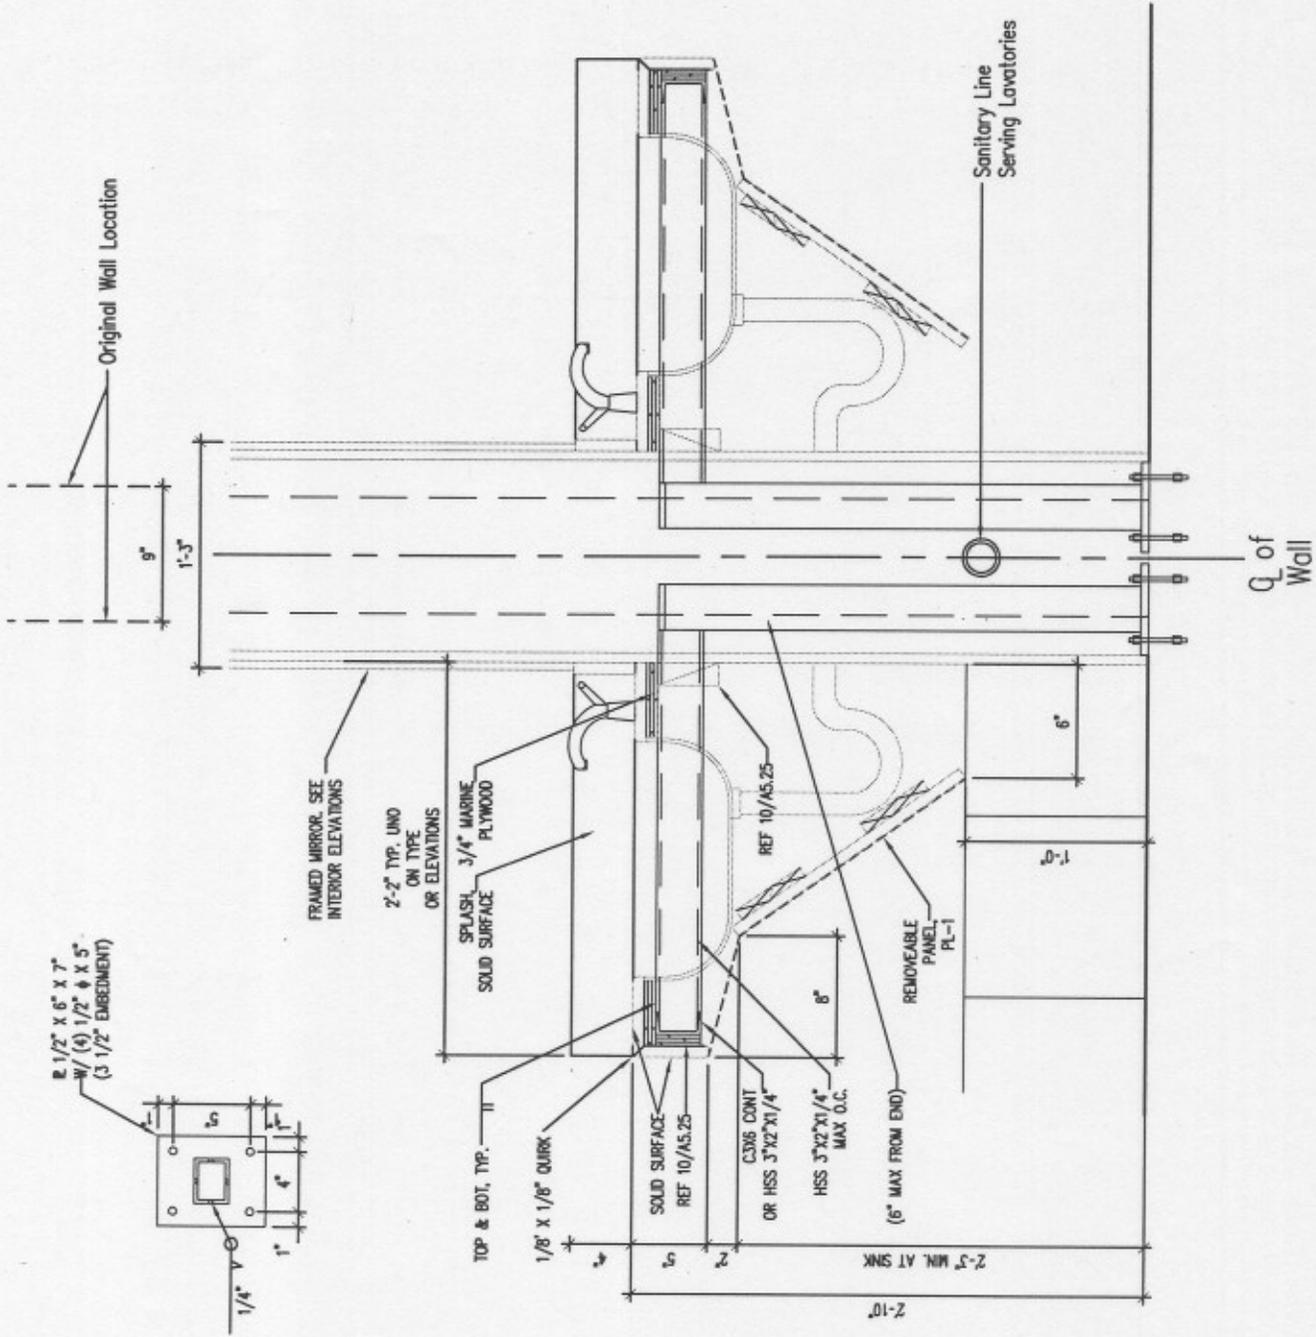

RFI 381
