



September 9, 2019

Brad Harris
Collin County Purchasing Department
2300 Bloomdale
McKinney TX 75071

Re: Myer Park Roof Replacement – Additional Foam Tear Out Change Order Request

Globus Management Group proposes to furnish labor, materials and equipment to complete the full scope of work on the above project. Quantities and scope of work listed below.

Multiple areas had saturated foam all the way down to the metal deck. The additional scope of work, not included in the contract was as follows:

Approximately 5,900 square feet in multiple areas listed on the attached roof drawing

Labor to remove additional wet foam
Clean the existing exposed metal decking/dry foam
Apply primer to the areas
Install multiple layers of foam to achieve a matching thickness to the existing foam
Then install new 1.5" foam system included in the base contract

Additional labor for entire scope on all areas	\$9,035.00
Additional materials for cleaner, primer & foam system	\$8,950.00
Additional dumpster	\$ 750.00
Additional rental time for skytrack & equipment staging	<u>\$1,850.00</u>
Sub-total	\$20,585.00
Additional profit per contract	<u>\$2,058.50</u>

Total Cost of Change Order


~~-\$23,443.50~~

**9/25/19 Revised
Amount \$22,643.50**

Additional Days required for completion:

NTP for original contract 5/7/19

Days included in contract 10 days plus 85 working days which brings us to 8/11/19

Approved by 

We require another 50 days for additional change order items.

This brings substantial completion to 8/10/19 & final completion to 9/30/19.

Please see attached roof plan with areas marked for additional work. Also see attached photos.

Respectfully Submitted,
Ken Edwards

X 

Dan DeMeyer
Drytec

X 


GLOBUS

MANAGEMENT GROUP

Collin County



Name _____

X _____

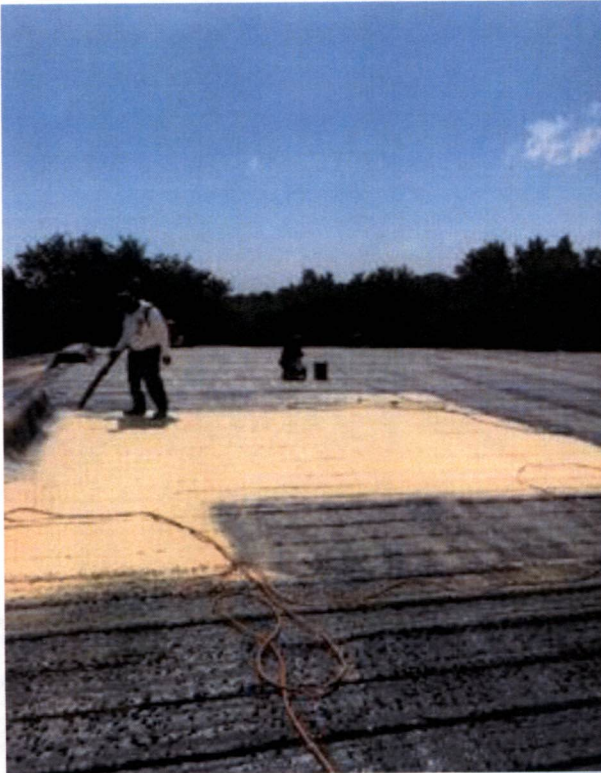

GLOBUS

MANAGEMENT GROUP

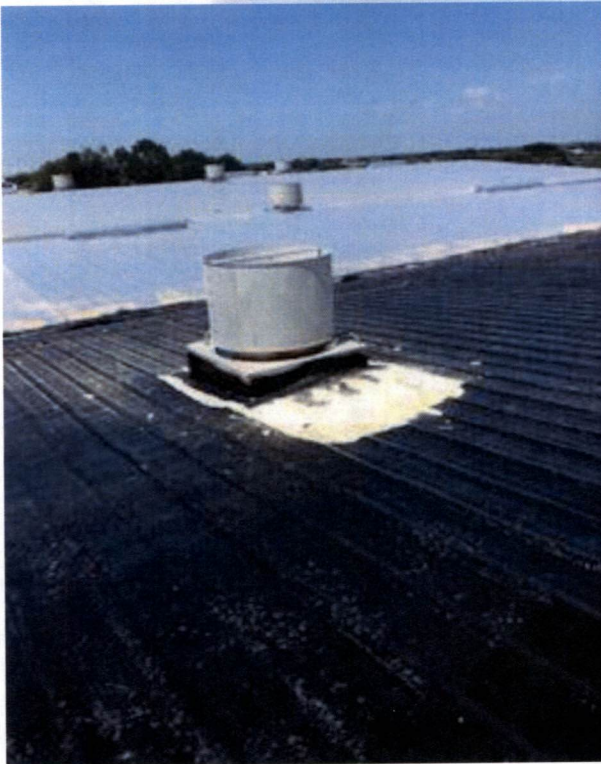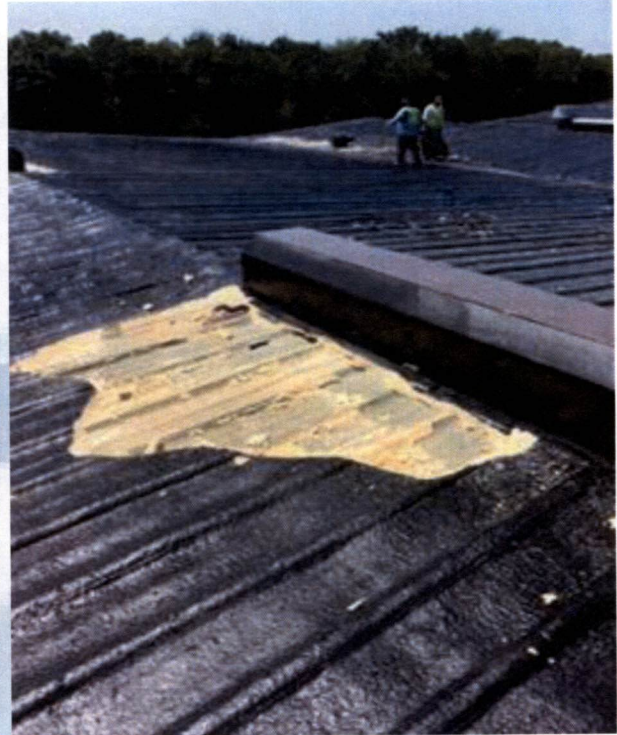

GL^oBUS

MANAGEMENT GROUP

